




Project: Facility Development Plan Date: Fri 10/08/01	Task		Milestone		Rolled Up Critical Task		Split	
	Critical Task		Summary		Rolled Up Milestone		External Tasks	
	Progress		Rolled Up Task		Rolled Up Progress		Project Summary	

ID	Task Name	Duration	2001												2002																						
			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S					
32	Specify optics & moun	2 wks																																			
33	parts procurement	144 days																																			
34	benches	15 wks																																			
35	imaging mirror	15 wks																																			
36	rest of steering	16 wks																																			
37	off-shelf optics	6 wks																																			
38	Beam steering system	109 days																																			
39	mount prototyping, 1-ε	4.4 wks																																			
40	Confirm steering hard	2 days																																			
41	Spec & write software	17 wks																																			
42	Test steering system	1 wk																																			
43	Imaging system	154 days																																			
44	prototype alignment sc	2 wks																																			
45	test/ re-work mirror	1 wk																																			
46	align & fix sources ref	1 wk																																			
47	set-up verification patl	1 wk																																			
48	full system	9 days																																			
49	full control-law test	1 wk																																			
50	System Completed	0 days																																			
51	Sources	288 days																																			
52	Laser Rebuild	54 days																																			
53	Clean up Equipment	2 wks																																			
54	Integration Procedure	1 wk																																			
55	Move Optics back to c	1 day																																			
56	Remount electronics	1 wk																																			
57	Reinstall Laser Interlo	2 wks																																			
58	Connect Vacuum Pump	1 wk																																			
59	Plumb in water	2 days																																			
60	Reinstall C02 Laser	1 wk																																			
61	Set up FIR Laser	2 wks																																			
62	Align Optics	2 days																																			

Project: Facility Development Plan Date: Fri 10/08/01	Task		Milestone		Rolled Up Critical Task		Split	
	Critical Task		Summary		Rolled Up Milestone		External Tasks	
	Progress		Rolled Up Task		Rolled Up Progress		Project Summary	

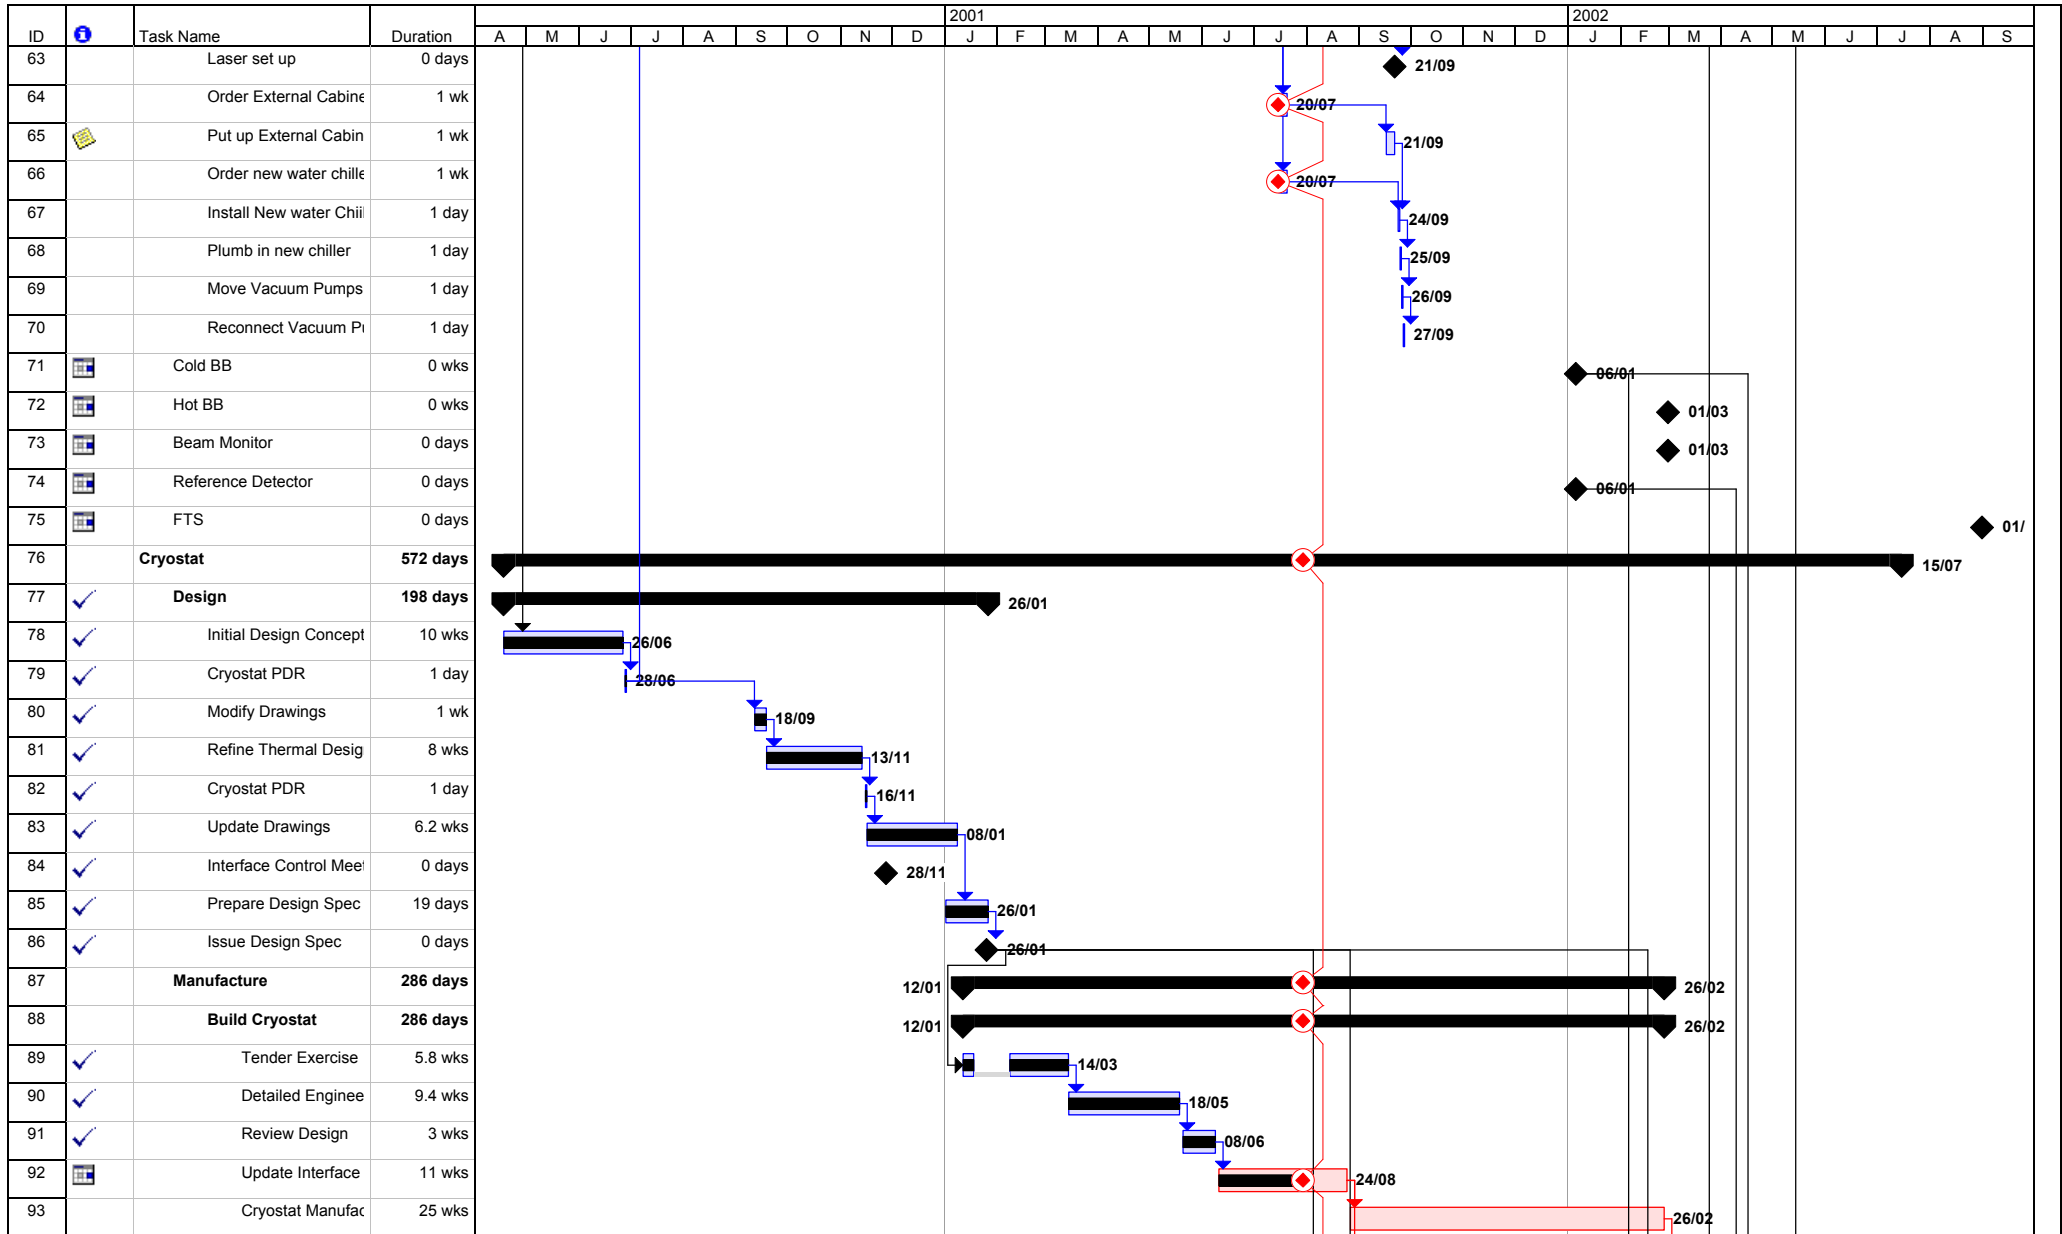

Project: Facility Development Plan
 Date: Fri 10/08/01

Task		Milestone		Rolled Up Critical Task		Split	
Critical Task		Summary		Rolled Up Milestone		External Tasks	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary	

